8TH STREET

Reconstruction Project

Minneapolis
City of Lakes

Construction Update

August 31 – September 14, 2018

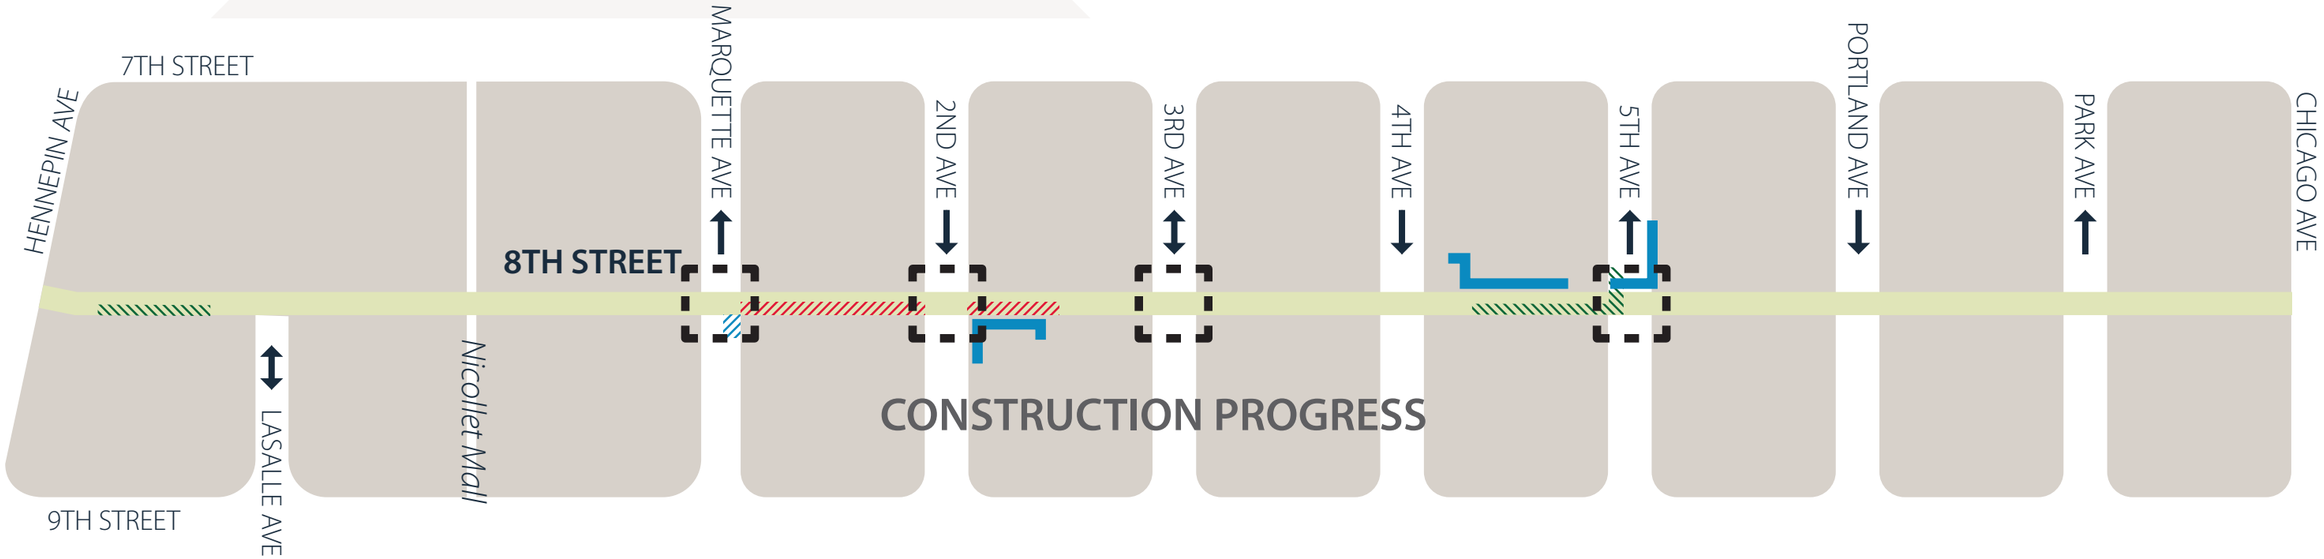

- Partial intersection reduction
- Full closure
- Xcel Energy
- City Sewer and Water
- Centerpoint Gas
- Telecommunications
- NRG
- Temporary water (removals)

WHAT'S HAPPENING

- Xcel Energy is upgrading existing manhole and duct facilities from Marquette Ave to 2nd Ave, and from 2nd Ave to 3rd Ave.
- Watermain lining work is completed. Crews will be removing temporary watermain from sidewalk areas over the next few weeks.
- Sanitary sewer lining between 5th Ave and Chicago Ave have been completed. Remaining lining work between 2nd Ave and 5th Ave will be completed in mid-September, and additional lining work east of Chicago Ave (outside the 8th St project limits) will be occurring the week of Labor Day.
- Comcast will be installing facilities in sidewalk areas between 3rd Ave and 5th Ave.
- Sprint will be potholing existing duct bank facilities between Hennepin Ave and Lasalle Ave

WHAT TO EXPECT

- Public and private utility work requiring the use of heavy equipment will increase noise, vibration, and dust in work areas.
- Vehicle traffic and congestion accompanying lane restrictions on 8th St. between Hennepin Ave and Chicago Ave. Anticipate one lane of traffic open weekdays between 9 AM and 3 PM, and two lanes open during weekday rush hours. Lane restrictions will vary by block based on construction activity.
- Intersection lane restrictions at 2nd Ave and Marquette Ave through late-September to accommodate 2nd Ave and Marquette Ave concrete repairs.
- Pedestrian detours as needed to facilitate construction needs. Greater impacts can be expected at intersections where work is occurring.
- Changes to Metro Transit bus stops as work progresses throughout the corridor. Bus service on 8th Street will remain during 2018, although temporary bus stop closures are anticipated.

STAY CONNECTED

- Visit the project website: *www.8thStreetProject.com*
- Sign up for project updates
- Email *info@8thStreetProject.com*
- Contact the project hotline with questions, comments or concerns: *612-404-1830*

8TH STREET
Reconstruction Project

Minneapolis
City of Lakes

Block-by-Block Work Summary
August 31 – September 14, 2018

8TH STREET BLOCK	PROJECT RELATED WORK	ANTICIPATED ROAD/PEDESTRIAN RESTRICTIONS				
		TEMPORARY PED RAMPS	PARKING RESTRICTIONS	TWO LANES OPEN (5-9 AM + 3-7 PM)	ONE LANE OPEN (NON-RUSH HOUR)	NOTES
8th St/Hennepin Ave Intersection						
Hennepin Ave to Lasalle Ave	Sprint Potholing (south side of roadway)			**X**		
Lasalle Ave to Nicollet Mall						
Nicollet Mall to Marquette Ave	Staging area for Xcel duct bank at Marquette Ave (south side)		**X**	**X**	**X**	
8th St/Marquette Ave Intersection	Fire Hydrant Relocation (SE Corner)		**X (on Marquette)**		**X**	- One northbound lane closed to facilitate hydrant relocation & restoration with Marquette concrete pavement repair
Marquette Ave to 2nd Ave	Xcel duct bank (south side) MCI (Verizon) conduit installation (with Xcel work)		**X**	**X**	**X**	
8th St/2nd Ave Intersection			**X**	**X**		- 2nd Ave concrete repair project
2nd Ave to 3rd Ave	Temporary watermain disassembly Xcel manhole installation/replacement		**X**	**X**	**X**	
8th St/3rd Ave Intersection	Comcast facility rehabilitation & expansion		**X (on 3rd Ave)**	**X (on 3rd Ave)**		
3nd Ave to 4th Ave	Comcast facility rehabilitation & expansion (sidewalk areas)		**X**	**X**		- Interim sidewalk closures with detours to opposite side between intersecting streets
8th St/4th Ave Intersection						
4th Ave to 5th Ave	Temporary watermain removal (north sidewalk) Comcast facility rehabilitation & expansion (sidewalk areas)		**X**	**X**		- Interim sidewalk closures with detours to opposite side between intersecting streets
8th St/5th Ave Intersection	Temporary watermain removal and restoration		**X (on 5th Ave)**	**X (on 5th Ave)**		- Interim pedestrian and bicycle lane restrictions at intersection
5th Ave to Portland Ave						
8th St/Portland Ave Intersection						
Portland Ave to Park Ave						
8th St/Park Ave Intersection						
Park Ave to Chicago Ave						
8th St./Chicago Ave Intersection						
